



# Jamestown Community Meeting

June 11, 2014



## Tonight's Agenda

- Announcements
- Volunteer Coordination
- Mennonite Disaster Services & Habitat for Humanity
- PPDR Demolition Program
- HMGP Buy-Out Program
- Boulder County Update
- Long-Term Recovery Plan Update
- Fire Station Update
- Emergency Watershed Protection Program
- Water Treatment Plant Update
- Water Distribution System & Roads Update



# **Announcements**

## **Jamestown Support Group**

- When: Wednesday, June 11<sup>th</sup>, 6:30pm-8:30pm
- Where: Jamestown Community Church
- What: A place to hold each other up while we deal with the natural response to trauma

Led by: Tamira Jenlink, MA

- Body-Centered / Nature
- Based Psychotherapist
- Mountain Vision Therapy

**All are welcome!**



# Announcements

## Boulder Municipal Airport Day

- When: Saturday, June 14th, 9:00-3:00
- Where: Boulder Municipal Airport
- What:
  - To Thank the **National Guard** and **US Army 4th Aviation Combat Brigade** for safely evacuating our Community in September!
  - Tour the aircraft used in the evacuation and Experimental aircraft
  - Formal Appreciation Ceremony: 12:00pm
  - Helicopter rides (for a fee)
  - ***Please sign Jtown cards for the troops and agencies attending***





## Volunteer Coordination Update

### Habitat for Humanity & Mennonite Disaster Services

- If you need work, please speak with Nina
- **Volunteers arriving in June!!!**
  - First group of volunteers are here
  - 20 volunteers arriving every Sunday through the summer or until we're out of work requests
  - Scheduling volunteers for work that is permitted and funded
  - Nina and Rebecca working hard to expedite the paperwork process for people who have requested repairs and need funding





# Recovery Update

## Boulder County Building Permits

- Boulder County Commissioners approved discounts
- Permits for new construction or major repair work to structures with verified damage from a declared disaster will be charged a reduced fee provided that:
  - The structure being rebuilt is the same or smaller than that which existed prior to the fire, and
  - The structures do not exceed 2,500 square feet for a residence and 530 square feet for an accessory structure. If you already obtained a permit, refunds are available





# **Recovery Update**

## **Jamestown Floodplain Development Permit**

You might need a Floodplain Development Permit if...

You are building or adding:

- fences
- decks
- walls
- treehouses
- hot tubs
- fill dirt or rocks
- private footbridges and bridges

**Please see our Certified Floodplain Administrator, Mark Williams**



# Recovery Update

## HMGP Buy-Out Program: Next Steps

Update: The State will cover the appraisal costs for all HMGP homes.

### Next Step

**May-June**      **Complete Home Appraisals – In Progress**

**July**            **Application Dues**

### **IMPORTANT**

***If you are participating in the buy-out program, do not demo your own home without written permission from the Town.***

Questions: Call (866) 953-2325 or Email [buyout@bouldercounty.org](mailto:buyout@bouldercounty.org)





# Recovery Update

## Private Property Debris Removal Program: Next Steps

For demolition and debris removal. Available to all eligible properties.

### Next Steps:

**June 18**

**Project Start**

**We will contact property owners first**

### **IMPORTANT**

***If you are participating in the buy-out program, do not demo your own home without written permission from the Town.***



# Recovery Update

## Emergency Asphalt Overlay

- Lefthand Canyon Drive, James Canyon Drive & Fourmile Canyon Drive
- Currently being designed – Will go to bid ASAP
  - Overlay work will begin ASAP after bids accepted – June or July 2014
  - Estimated Projected Cost = \$1,000,000 to \$2,000,000



## Long-Term Recovery Planning






## Long-Term Recovery Planning

<u>Due</u>	<u>Activities</u>	<u>Status</u>
May 17	Release of RFP	Complete
June 4	Bidder Acknowledgement	Complete
June 6	Questions Due	Complete
June 10	Responses Distributed to All Bidders	Complete
June 18	Proposals Due Date by 5 pm	
June 23	Board review of proposals	
Week of June 23	Interviews	
June 30	Contract Award	
Sept 30	Completion Date	





## JVFD Fire Hall Reconstruction

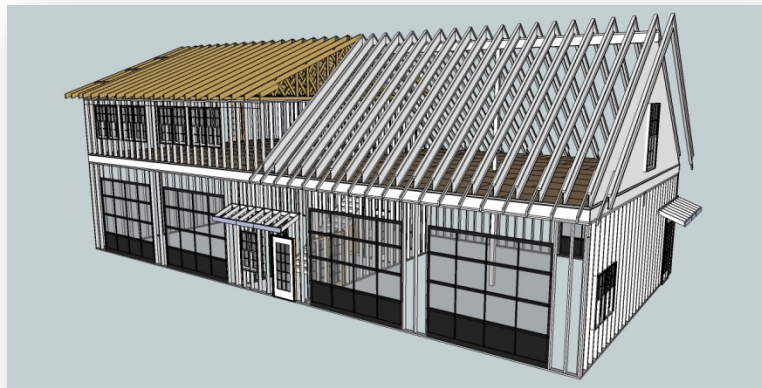

Due	Activities	Status
Apr 28	Confirm CIRSA funds	Complete
Apr 28	Confirm FEMA funds	Complete
May 1	RFP Draft Preparation	Complete
May 8	RFP Final Version	Complete
May 22	RFP Advertisement	Complete
May 29	Mandatory Site Visit	Complete
May 30	Questions Due	Complete
Jun 3	Addendum	Complete
Jun 12	Proposals Due	
Jun 16-17	Town Board & Interviews	
Jun 19	DOLA Grant Application Submission	
	Next Steps....	







## JVFD Fire Hall – Temporary Building





## JVFD Fire Hall – Temporary Building








# Emergency Watershed Protection

## AMEC and Colt & Steel

- Remaining work: touch ups, Loving's gulch, Howlett's gulch

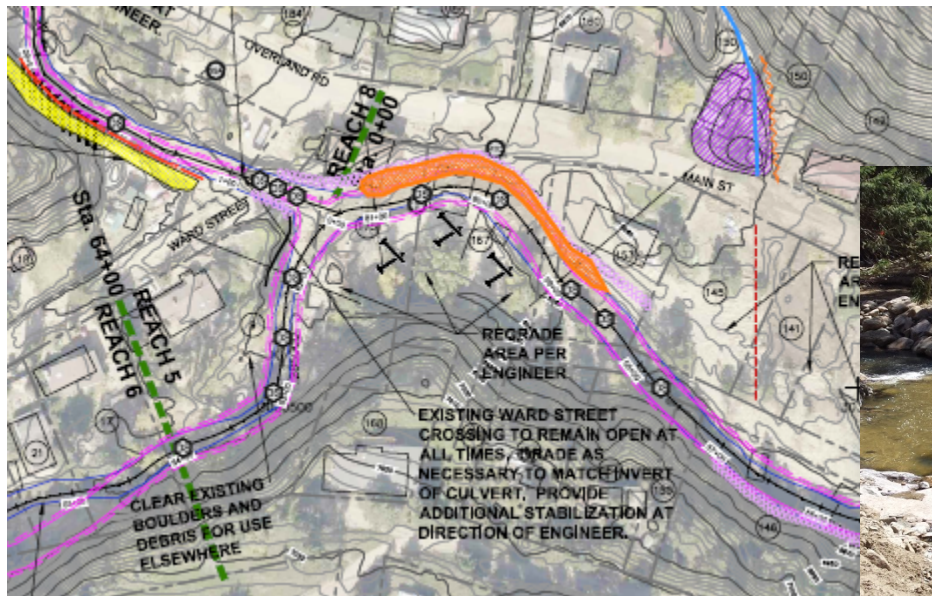



# Jamestown Water Distribution System

## Individual Service Lines

- **Updates:**
  - FEMA approved lowering 10' of service line
  - Destroyed service lines may be eligible under Individual Assistance
    - Assessment on progress

## Septic Systems

- **Updates:**
  - If your system was damaged or destroyed, please let us know.
  - Please also ensure your case manager knows
  - Same is true for wells!

# Jamestown Water Treatment Plant



## Filter Media Removal and Replacement

Date	Activity	Status
Apr 4	Phase 1: Sand & Underdrain Removal	Complete
May 16	Phase 1: Crack Repair	Complete
May 16	Phase 1: Temporary Intake Install	In Progress
Jun 2	Phase 1: Media Replacement	In Progress
Jun 27	Phase 1: Plant Start Up	

# Water Distribution, Road and Bridge

- Scope
  - Restore Water Distribution System and Service Connections (Phase 1)
  - Repair Roadways and Culverts (Phase 1)
    - 12<sup>th</sup> St from Lower Main St to Forest Service
    - Lower Main St
    - Ward St
  - Anderson Hill Bridge and Wall (Phase 2)
    - Replace Roadway Bridge
    - New Roadway Alignment due to James Creek shift



## Water Distribution, Road and Bridge

- Duran Construction Inc. (DEI)
  - Mobilizing Continues
  - Multiple Crews
  - Water Line to Mesa Street is
    - Temporary Crossing

## Water Distribution, Road and Bridge

- Activating the Water System
  - Existing Service Line
    - Turn off all faucets/hoses
    - Turn off at the Street
  - New Service Line Connections
    - Contractor will flush service line
    - Turn off all faucets/hoses
- DEI & Jamestown will Coordinate Timing

# Water Distribution and Roadway - Schedule

Duration	Activity	Status
Jun 5-20	Construction of temporary water line from WTP to Mesa St Restoration of the Town's water tanks	Complete
Jun 5-13	Replacement of the WTP sand filters	Complete
Jun 28	Activation of the water lines on Mesa, Spruce, 16th, Pine, Porphyry, Gillespie	In Progress
Jun 14-27	Construction of the water line and Ward St	
Jun 28	Activation of the water line on Ward St	
Jun 25-Jul 16	Construction of the water line and Main St (Ward to JVFD)	
Jul 18	Activation of the water line on Main St (Ward to JVFD)	
Jul 9-22	Construction of the water line on High St and 15th St	
Jul 23	Activation of the water line on High St and 15th St	
Jul 17-Aug 3	Construction of the water line on Lower Main St and 12 <sup>th</sup>	
Aug 4	Activation of the water line on Lower Main St and 12 <sup>th</sup>	
Jun 30-Jul 29	Construction of Ward St Box Culvert	
TBD	Construction of Gillespie Gulch Culvert (being redesigned)	
TBD	Construction of permanent water line from WTP to Mesa St	

## Anderson Hill Road

- Data Gathering is Complete
  - Alignment Study Completed and Approved
  - Geotechnical Investigations
  - Survey
- Next Steps
  - Size Bridge
  - Wall Geometry
  - Finalize Roadway Geometry

# Anderson Hill Bridge and Wall (Phase 2)- Schedule

Date	Activities	Status
Fri, Feb 28	Design Team site visit	Complete
April	Preliminary Roadway Alignment	Complete
April	Conceptual Design	Complete
May 6	Community Meeting to Discuss Bridge	Complete
July 9	Community Meeting to Discuss Wall Types & Bridge Selection	
July 23	Community Meeting – Design Update	
July	Design Approval by FEMA	
September	Design Completed	
October	Construction Begins	
January	Construction Completed (Estimate)	

# Permanent Repairs to Water Treatment Plant

Date	Activities	Status
Mon, Apr 24	Signed Contract	Complete
Fri, May 9	Bore for Soils Report	Complete
Fri, May 16	Complete Design Criteria	Complete
Fri, June 6	Complete Final Design/Bid Documents	Complete
Wed, Jun 11	Advertise for Bids	Complete
Fri, Jun 20	Receive Bids	
Mon, Aug 4	Operation of WTP Begins	
September	Finish Construction	
